Construction Hot Topics

Week of: April 23, 2017 - April 29, 2017

1. Terminal 7: Departures to Baggage Claim

- A new escalator that provides down transportation from Terminal 7's Concourse to Baggage Claim has opened. Deplaning passengers can now expediently access the baggage claim via this new escalator (both images below).
- Terminal 7's new Bag Claim 1 carousel is complete, and will be operating by the end of May.



2. Terminal 7: Departures Level


• The current phase of construction in Terminal 7's Departures level includes work on the hallway (left image) that overlooks the Ticketing level and Security Check-point. This is also the hallway that connects Terminal 7 and Terminal 8. Since this hallway is closed for construction, passengers are rerouted through the north end of the concourse, past the new Customer Service station adjacent to Gate 70A (right image), and into the Terminal 8 hallway.



(continued on next page)



- 3. CTA: Upper Level: As Reported Week of 12.12.16; new information is highlighted
 - The security bollards for the Upper Level Roadway doors will begin December 12 and continue through June 2017. Working hours are between 11PM – 8AM, but barricades will be in place 24/7.
 - The final set of nine bollards (image below) associated with the project's current scope of work
 was installed in Terminal 1 last week adjacent to doors T1-L2-05, 06. Remaining work includes
 adding the stainless steel sleeves and tops (dome tops to all but the removable bollard in each
 set, which receives a flat top).

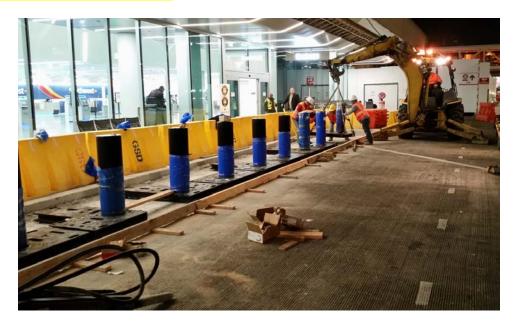

- 4. Terminal 3: Delta Move
 - With the May airline terminal shuffle fast approaching, efforts to have Delta moved in at Terminal 3 are underway on all levels. Check-in kiosks have been installed (left image), on Ticketing and a new set of FIDs is nearly complete (right image) on Arrivals.



