
# **Construction Hot Topics**


Week of February 3, 2020

### 1. Terminal 2: Starbucks Construction Extended

 Construction barricades in the Terminal 2 concourse that were originally scheduled to be removed this week will now be in place through late March 2020 while a new Starbucks

concession is finished



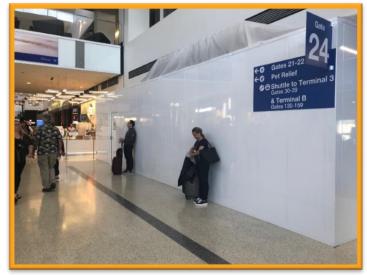



APM falsework on Center Way

### 2. Automated People Mover Construction Milestone

- The APM project recently reached a big milestone with the erection of falsework on Center Way between Parking Structures 1 and 7
- Falsework (combination of steel and lumber, pictured above) is a temporary structure that's needed to support permanent structures until construction is far enough along to support itself





# **Construction Hot Topics**

Week of February 3, 2020

## 3. Bridge Demolition Completed: Parking Structure 2A / 2B

- The Automated People Mover project has completed the demolition of the connecting bridge between Parking Structures 2A and 2B
- Activity will continue this week to clean up minor debris and the overall worksite

PS-2A / PS-2B bridge demolition





Northbound West Way is closed to maintain southbound West Way traffic during APM

### 4. Northbound West Way: Closed through June 1, 2020

- Northbound West Way from World Way South to World Way North is through Monday, June 1,
  2020 at 7AM for Automated People Mover construction
- Southbound traffic on West Way, Parking Structure 2B egress, and pedestrian traffic is maintained



